

# SWARM EX COMMs

Sep 23, 2026

<http://>

Project manager

Project dates

Sep 9, 2026 - Nov 28, 2026

Completion

6%

Tasks

40


Resources

0

## Tasks

| Name                                                                  | Begin date | End date |
|-----------------------------------------------------------------------|------------|----------|
| Gpredict                                                              | 9/9/26     | 11/3/26  |
| Create motor test plan                                                | 9/9/26     | 9/14/26  |
| Checking remaining things to raise antenna                            | 9/15/26    | 9/17/26  |
| Rooftop prereqs: LNA, lightning arrestors, antenna installs (delayed) | 9/23/26    | 10/1/26  |
| Executin motor tests                                                  | 10/2/26    | 10/12/26 |
| Raising antenna                                                       | 10/13/26   | 10/16/26 |
| finding exact location of ground station                              | 9/16/26    | 9/23/26  |
| g predict tracking with TLEs                                          | 9/24/26    | 9/30/26  |
| interface gnu with g predict                                          | 10/1/26    | 10/7/26  |
| testing sat tracking                                                  | 10/26/26   | 11/3/26  |
| Hydra Lithium Communication                                           | 9/16/26    | 10/22/26 |
| MCT: Review test docs                                                 | 9/16/26    | 9/16/26  |
| MCT: Develop Hydra for MCT                                            | 9/23/26    | 9/29/26  |
| MCT: Bench setup                                                      | 9/30/26    | 10/1/26  |
| MCT: Practice run-through of test                                     | 10/2/26    | 10/2/26  |
| MCT: Full run through of test                                         | 10/5/26    | 10/6/26  |
| MCT: Troubleshooting                                                  | 10/7/26    | 10/7/26  |
| SCT-1: Review test docs                                               | 10/8/26    | 10/8/26  |
| SCT-1: Develop Hydra for SCT-1                                        | 10/9/26    | 10/15/26 |
| SCT-1: Bench setup                                                    | 10/16/26   | 10/16/26 |
| SCT-1: Practice run-through of test                                   | 10/19/26   | 10/19/26 |
| SCT-1: Full run through of test                                       | 10/20/26   | 10/21/26 |
| SCT-1: Troubleshooting                                                | 10/22/26   | 10/22/26 |
| Ground Station PC Architecture                                        | 9/23/26    | 10/27/26 |
| ON HOLD: Palo reviewing lab machines                                  | 9/23/26    | 9/29/26  |
| Transferring HFSS to new 443 machine                                  | 9/30/26    | 10/1/26  |
| Setting up laptop for GND station                                     | 10/2/26    | 10/12/26 |
| Connecting laptop and 443 machine                                     | 10/13/26   | 10/16/26 |
| Verify ground station arch with current setup                         | 10/19/26   | 10/23/26 |
| Planning final GND station architecture                               | 10/26/26   | 10/27/26 |
| Running SCT-2                                                         | 10/23/26   | 11/27/26 |
| Review SCT2 procedure                                                 | 10/23/26   | 10/26/26 |
| SCT-2: Develop Hydra for SCT-2                                        | 10/27/26   | 11/2/26  |
| Reverify Hydra-Li Comms                                               | 11/3/26    | 11/5/26  |
| Reverify GND station setup                                            | 11/6/26    | 11/10/26 |
| Bench setup                                                           | 11/11/26   | 11/12/26 |
| Practice run-through of SCT-2                                         | 11/13/26   | 11/16/26 |
| Full SCT2 runthrough                                                  | 11/17/26   | 11/20/26 |
| Testing and troubleshooting                                           | 11/23/26   | 11/25/26 |
| Post-test documentation review                                        | 11/26/26   | 11/27/26 |

Gantt Chart

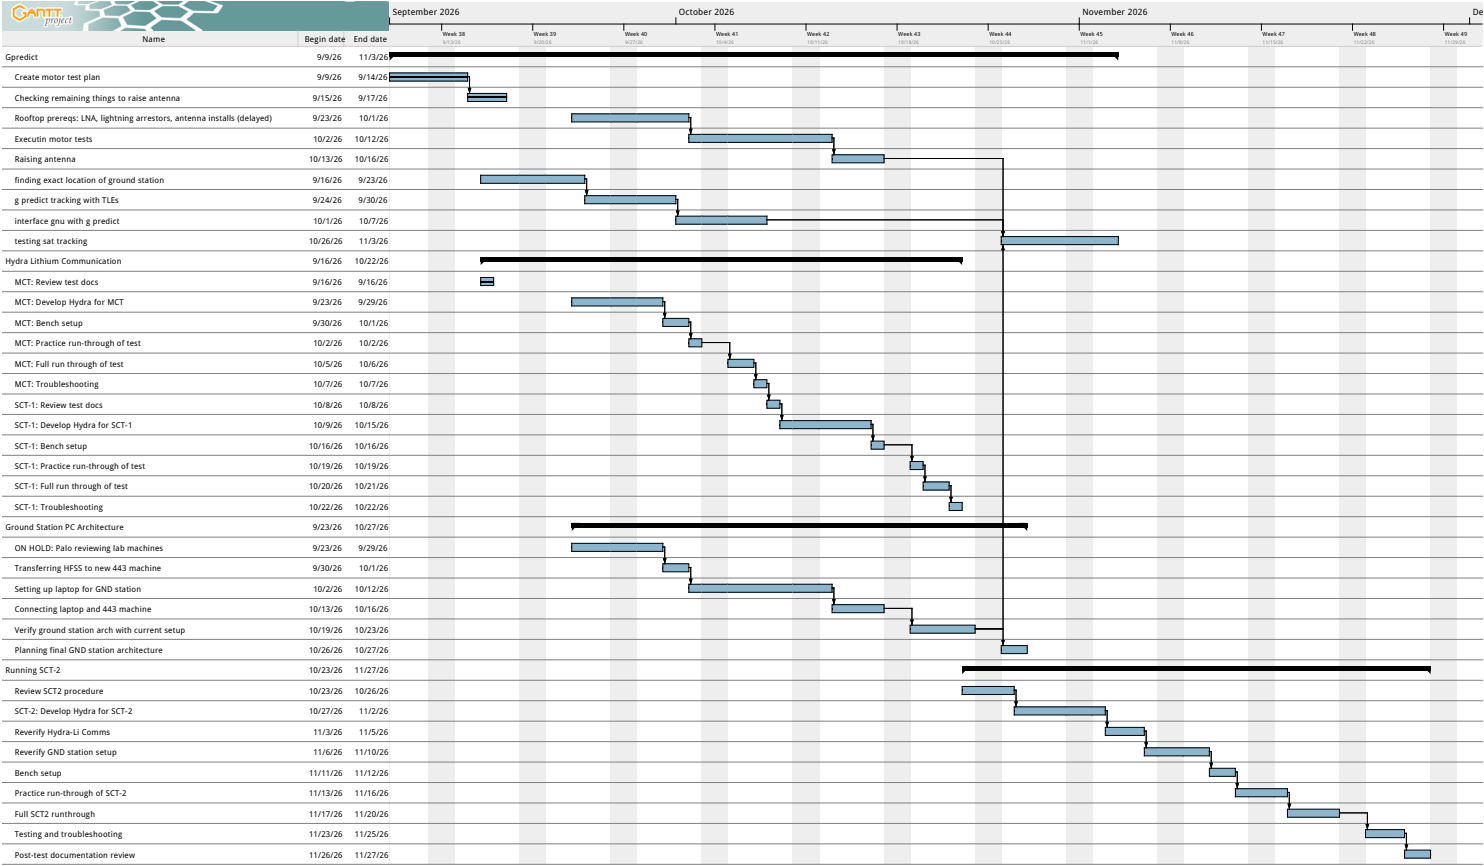

|      |              | September 2026     |                    |                    | October 2026       |                     |                     |                     | November 2026      |                    |                     |                     |                     | De |
|------|--------------|--------------------|--------------------|--------------------|--------------------|---------------------|---------------------|---------------------|--------------------|--------------------|---------------------|---------------------|---------------------|----|
| Name | Default role | Week 38<br>9/13/26 | Week 39<br>9/20/26 | Week 40<br>9/27/26 | Week 41<br>10/4/26 | Week 42<br>10/11/26 | Week 43<br>10/18/26 | Week 44<br>10/25/26 | Week 45<br>11/1/26 | Week 46<br>11/8/26 | Week 47<br>11/15/26 | Week 48<br>11/22/26 | Week 49<br>11/29/26 |    |
