






Accomplishments	Issues Impeding Progress			
- MCT completed - ran on Thursday with Saanika - commands were acknowledged correctly - Found out that the UART port connected to had TX and RX swapped - Test documentation recorded and updated - Looking into SCT1	None			
Plan for the Week	Upcoming Deliverables	Planned	Revised	Remaining
- Working with CDH for a practice run through of SCT1 to find out what is missing - Update with latest GNU version and first pass at seeing what state it is in for SCT 2	Re run MCT	9/21	10/5	0hr
	Re run SCT 1	9/30	10/20	24hrs
	Ground Station PC test	9/23	10/23	22hrs

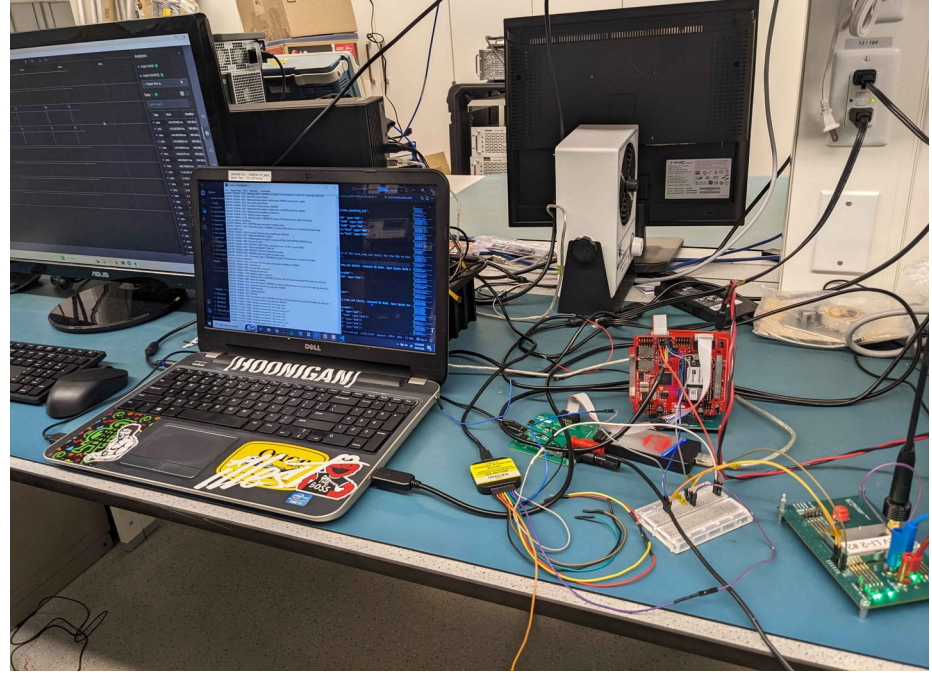


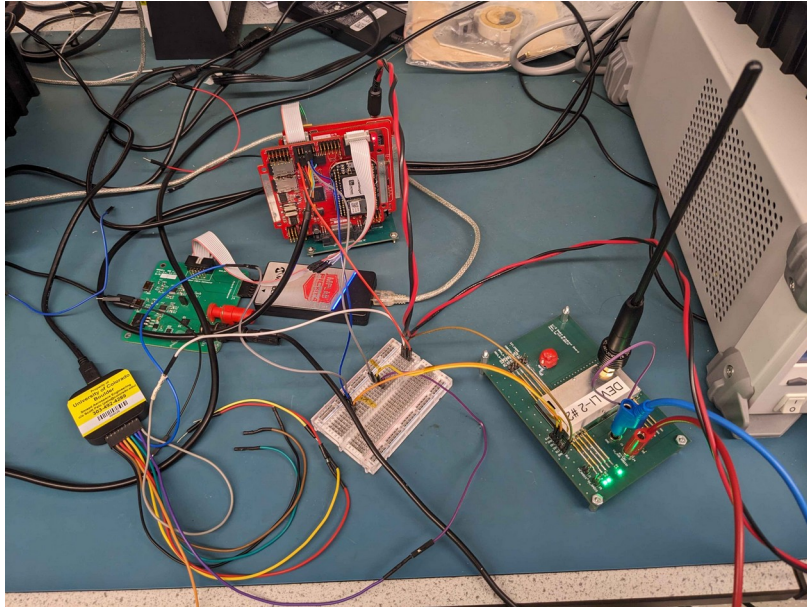


Test setup

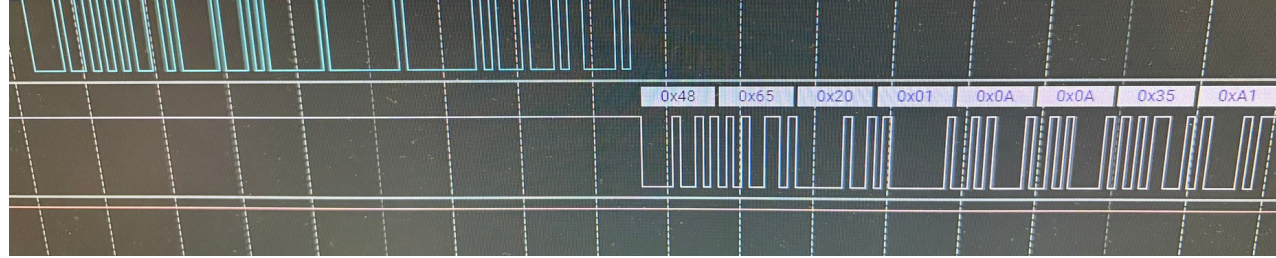

li2 no op

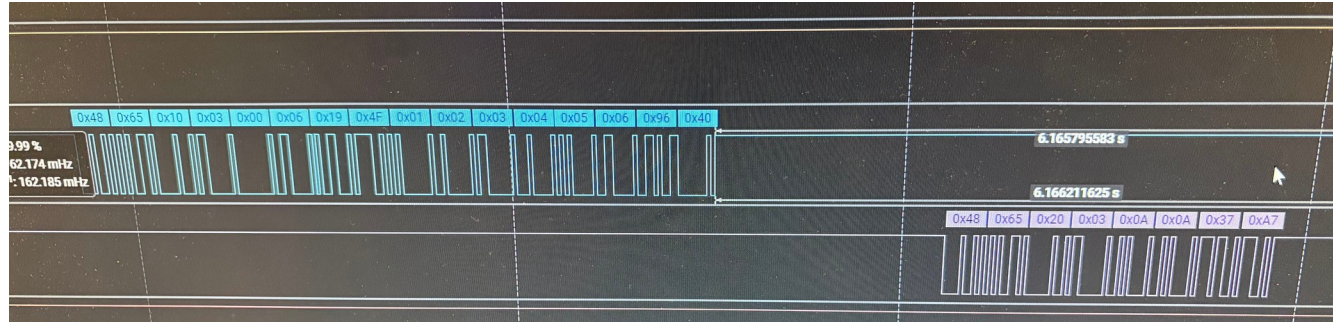

li2 transmit

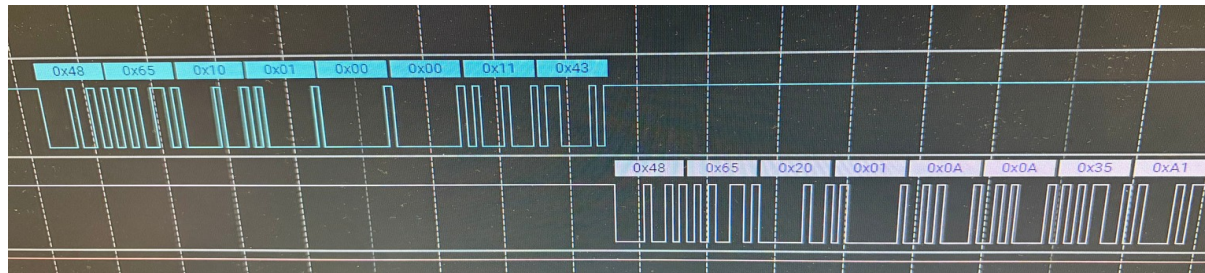

li2 reset

		Total Hours		Week Start Date																	Status
		Estimated	Actual	8/24	8/31	9/7	9/14	9/21	9/28	10/5	10/12	10/19	10/26	11/2	11/9	11/16	11/23	11/30	12/7	12/14	
Class & Meetings		31%	87	61.5	14	8	10	8	7	6.5	0	0	0	0	0	0	0	0	0	0	
Class	Lecture	35	21	3	3	3	3	3	3	3	0	0	0	0	0	0	0	0	0	0	Not Started
	Lecture	15	7	1	1	1	1	1	1	1											Ontime (In Progress)
	Lab	20	14	2	2	2	2	2	2	2											Ontime (In Progress)
Meetings		33	25.5	4	3	3	3	5	4	3.5											Ontime (In Progress)
	Lab	9	7	1	1	1	1	1	1	1											Ontime (In Progress)
	Full Team Mtg	12	7	1	1	1	1	1	1	1											Ontime (In Progress)
	Subsys Meeting	12	11.5	2	1	1	1	3	2	1.5											Ontime (In Progress)
Project Prep		15	15	7	2	4	2														Ontime (In Progress)
	Complete Paperwork	3	3	3																	Ontime (In Progress)
	Read Documents	12	12	4	2	4	2														Ontime (In Progress)
Reviews		4	0																		Not Started
	Mid Sem Review	2	0																		Not Started
	EOS Review	2	0																		Not Started
Documentation		22%	62	9	1	2	2	1	1	1	1	0	0	0	0	0	0	0	0	0	
Semester Planning		4	4	1	2	1															Complete
	SOW	2	2	1	1																Complete
	Personal Plan	2	2		1	1															Complete
Weekly Reporting		6	5			1	1	1	1	1											Not Started
	Quadcharts	6	5			1	1	1	1	1											Not Started
Review Prep		15	0																		Not Started
	Mid Sem Review	5	0																		Not Started
	EOS Review	10	0																		Not Started
Final Report		37	0																		Not Started
	Draft	15	0																		Not Started
	Final Report	22	0																		Not Started
Technical		46%	129	43	0	2	3	7	8	15	8	0	0	0	0	0	0	0	0	0	
MCT: Hydra Lithium Communication		26	26			1	2	4	13	6											Not Started
	MCT: Review test docs	1	4			1		1	2												Complete
	MCT: Bench setup	2	3					1	2												Complete
	Learning Hydra	4	2						2												Complete
	MCT: Hydra development	4	4						4												Complete
	MCT: Hydra hardwired to Li2	4	4						4												Complete
	MCT: Hydra hardwired to CDH to Li2	4	2						2												Complete
	MCT: Practice run-through of test	2	2						1	1											Late & Complete
	MCT: Full run through of test	3	3							3											Complete
	MCT: Troubleshooting	2	2							2											Complete
	SCT-1: Hydra Lithium Communication	15	2							2											Not Started
	SCT-1: Review test docs	1	2							2											Not Started
SCT-1: Hydra Lithium Communication	SCT-1: Bench setup	2	0																		Not Started
	SCT-1: Hydra development	5	0																		Not Started
	SCT-1: Practice run-through of test	2	0																		Not Started
	SCT-1: Full run through of test	3	0																		Not Started
	SCT-1: Troubleshooting	2	0																		Not Started
																					Not Started
																					Not Started
																					Not Started
																					Not Started
																					Not Started
Ground Station PC Architecture		31	7		2	2	1	2													Not Started
	Setting up laptop for GND station	8	1				1														Ontime (In Progress)
	Connecting GND station with GND station se	5	0																		Not Started
	Verify ground station arch with current setup	8	0																		Not Started
	Planning final GND station architecture	10	6		2	2		2													Ontime (In Progress)
Running SCT-2		37	0																		Not Started
	Review SCT2 procedure	2	0																		Not Started
	SCT-2: Develop Hydra for SCT-2	5	0																		Not Started
	Reverify Hydra-Li Comms	5	0																		Not Started
	Reverify GND station setup	5	0																		Not Started
	Bench setup	3	0																		Not Started
	Practice run-through of SCT-2	3	0																		Not Started
	Full SCT2 runthrough	6																			Not Started
	Testing and troubleshooting	5	0																		Not Started
	Post-test documentation review	3	0																		Not Started
Management		20	8				4	4													Not Started
	Onboarding	5	4				2	2													Not Started
	Documentation review	15	4				2	2													Not Started
TOTALS:		278	113.5	15	12	15	16	17	23	15.5											
Target		240	240	15	15	15	15	15	15	15	15	15	15	15	15	15	0	15	15	15	
Difference		-38	126.5	0	3	0	-1	-2	-8	-0.5	15	15	15	15	15	15	0	15	15	15	

Comment

Legend	
baseline (UNDO)	#
CHANGE	#
Re-Baseline	#
Complete	#
Completed early	#
Late	#
Very Late	#

indicates # of hrs worked

Not Started	Not Started
Completed	Complete
Completed early	Early
Ontime and in progress	Ontime
Late <1wk	Late
Late >1wk	Very Late

Notes	
If a task gets removed, use knockout (alt+shift+5) so that it is still visible	
If a task gets rebaselined just add a RB square but also leave the original baseline marker	
