

**Accomplishments**

- Hydra development
- Hardwired Hydra into Lithium for verification
 - still need CDH in the loop but this shows commands are working properly
- Started doc for the STIG ground station PC

Issues Impeding Progress


- CDH development
- Hydra development

Plan for the Week

- Work with CDH to fix how command byte is being read in, wrap up MCT
- Updating MCT documentation
- Prepare for re running SCT
- Move forward on testing two gs pcs to see if it helps hydra crashes

Upcoming Deliverables	Planned	Revised	Remaining
Re run MCT	9/21	10/5	8hrs
Re run SCT 1	9/30	10/20	30hrs
Ground Station PC test	9/23	10/23	26hrs




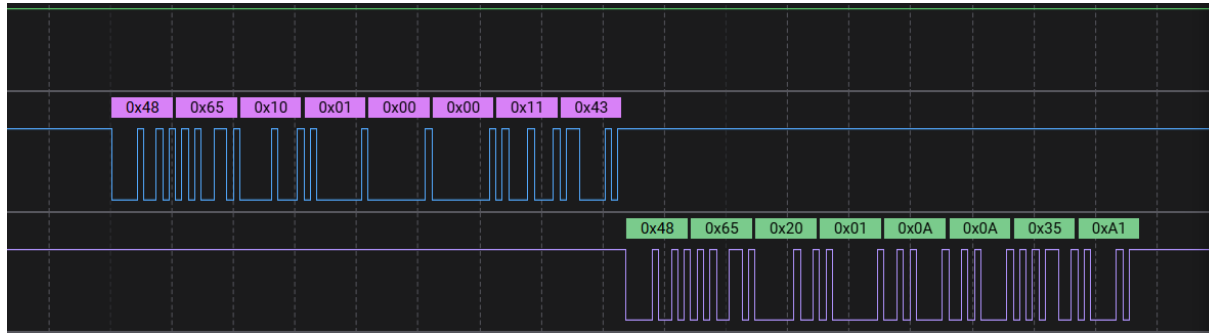

li2 no op



li2 transmit

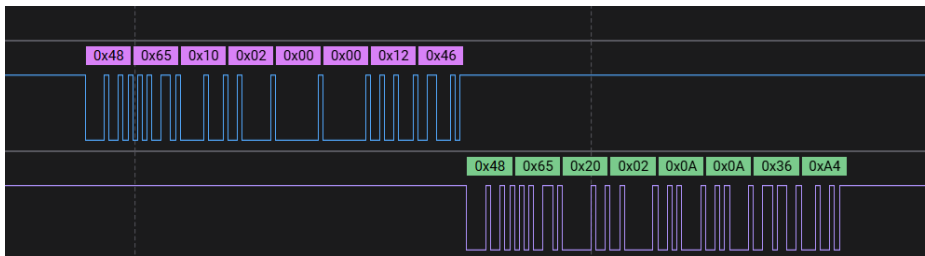

li2 reset

		Total Hours		Week Start Date																	Status
		Estimated	Actual	8/24	8/31	9/7	9/14	9/21	9/28	10/5	10/12	10/19	10/26	11/2	11/9	11/16	11/23	11/30	12/7	12/14	
Class & Meetings		31%	87	55	14	8	10	8	7	0	0	0	0	0	0	0	0	0	0	0	
Class	Lecture	35	18	3	3	3	3	3	3	0	0	0	0	0	0	0	0	0	0	0	Not Started
	Lecture	15	6	1	1	1	1	1	1												Ontime (In Progress)
	Lab	20	12	2	2	2	2	2	2												Ontime (In Progress)
Meetings		33	22	4	3	3	3	5	4												Ontime (In Progress)
	Lab	9	6	1	1	1	1	1	1												Ontime (In Progress)
	Full Team Mtg	12	6	1	1	1	1	1	1												Ontime (In Progress)
	Subsys Meeting	12	10	2	1	1	1	3	2												Ontime (In Progress)
Project Prep		15	15	7	2	4	2														Ontime (In Progress)
	Complete Paperwork	3	3	3																	Ontime (In Progress)
	Read Documents	12	12	4	2	4	2														Ontime (In Progress)
Reviews		4	0																		Not Started
	Mid Sem Review	2	0																		Not Started
	EOS Review	2	0																		Not Started
Documentation		22%	62	8	1	2	2	1	1	1	0	0	0	0	0	0	0	0	0	0	
Semester Planning		4	4	1	2	1															Complete
	SOW	2	2	1	1																Complete
	Personal Plan	2	2		1	1															Complete
Weekly Reporting		6	4			1	1	1	1												Not Started
	Quadcharts	6	4			1	1	1	1												Not Started
Review Prep		15	0																		Not Started
	Mid Sem Review	5	0																		Not Started
	EOS Review	10	0																		Not Started
Final Report		37	0																		Not Started
	Draft	15	0																		Not Started
	Final Report	22	0																		Not Started
Technical		46%	129	35	0	2	3	7	8	15	0	0	0	0	0	0	0	0	0	0	
MCT: Hydra Lithium Communication		26	20			1	2	4	13												Not Started
	MCT: Review test docs	1	4		1		1	2													Complete
	MCT: Bench setup	2	3				1	2													Complete
	Learning Hydra	4	2						2												Complete
	MCT: Hydra development	4	4						4												Complete
	MCT: Hydra hardwired to Li2	4	4						4												Complete
	MCT: Hydra hardwired to CDH to Li2	4	2						2												Late (In Progress)
	MCT: Practice run-through of test	2	1						1												Not Started
	MCT: Full run through of test	3	0																		Not Started
	MCT: Troubleshooting	2	0																		Not Started
	SCT-1: Hydra Lithium Communication	15	0																		Not Started
	SCT-1: Review test docs	1	0																		Not Started
	SCT-1: Bench setup	2	0																		Not Started
	SCT-1: Hydra development	5	0																		Not Started
	SCT-1: Practice run-through of test	2	0																		Not Started
	SCT-1: Full run through of test	3	0																		Not Started
	SCT-1: Troubleshooting	2	0																		Not Started
Ground Station PC Architecture		31	7		2	2	1	2													Not Started
	Setting up laptop for GND station	8	1				1														Ontime (In Progress)
	Connecting GND station with GND station se	5	0																		Not Started
	Verify ground station arch with current setup	8	0																		Not Started
	Planning final GND station architecture	10	6		2	2		2													Ontime (In Progress)
Running SCT-2		37	0																		Not Started
	Review SCT2 procedure	2	0																		Not Started
	SCT-2: Develop Hydra for SCT-2	5	0																		Not Started
	Reverify Hydra-Li Comms	5	0																		Not Started
	Reverify GND station setup	5	0																		Not Started
	Bench setup	3	0																		Not Started
	Practice run-through of SCT-2	3	0																		Not Started
	Full SCT2 runthrough	6																			Not Started
	Testing and troubleshooting	5	0																		Not Started
	Post-test documentation review	3	0																		Not Started
Management		20	8				4	4													Not Started
	Onboarding	5	4				2	2													Not Started
	Documentation review	15	4				2	2													Not Started
TOTALS:		278	98	15	12	15	16	17	23								0	15	15	15	
Target		240	240	15	15	15	15	15	15	15	15	15	15	15	15	15	0	15	15	15	
Difference		-38	142	0	3	0	-1	-2	-8	15	15	15	15	15	15	15	0	15	15	15	

Comment

Legend	
baseline (UNDO)	#
CHANGE	#
Re-Baseline	#
Complete	#
Completed early	#
Late	#
Very Late	#

indicates # of hrs worked

Not Started	Not Started
Completed	Complete
Completed early	Early
Ontime and in progress	Ontime
Late <1wk	Late
Late >1wk	Very Late

Notes	
If a task gets removed, use knockout (alt+shift+5) so that it is still visible	
If a task gets rebaselined just add a RB square but also leave the original baseline marker	
